Kings Pond Outline Programme

DRAFT 6 July 26 - will be updated as project evolves
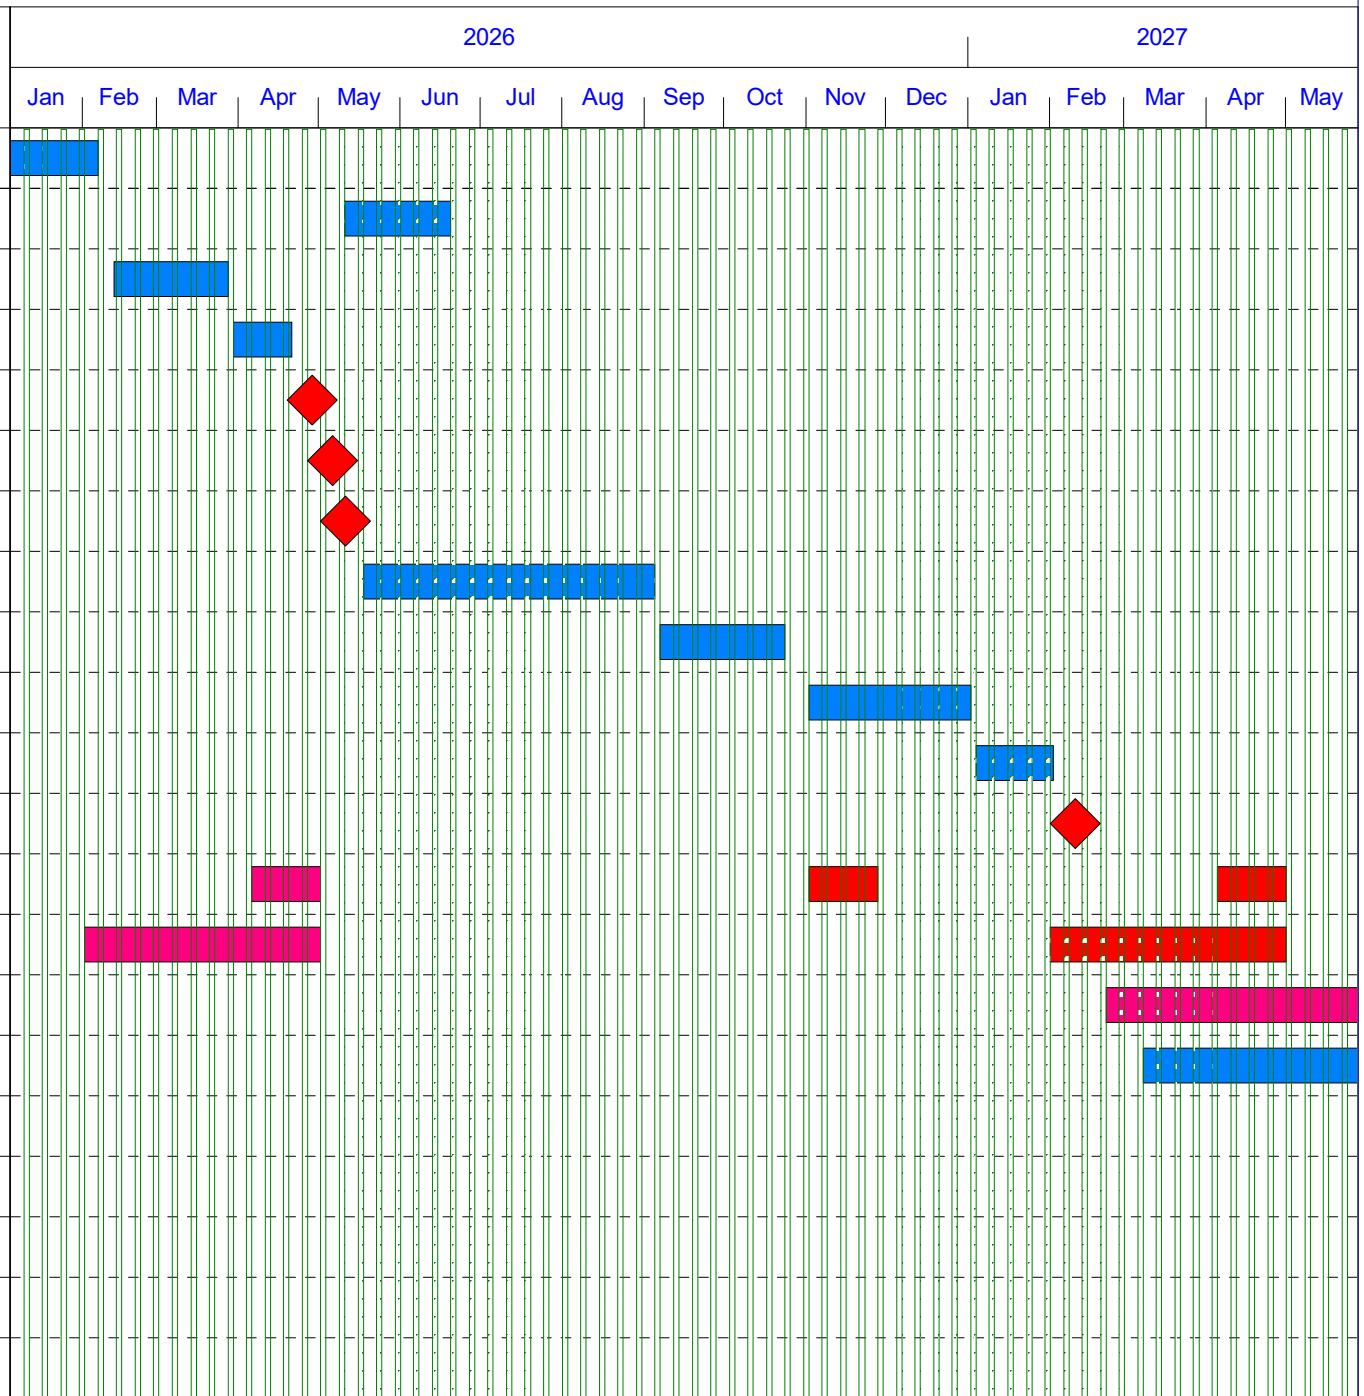
Finish	ID	Name	Duration
06/02/26	1	Gather Information	53w
19/06/26	2	Ecology Surveys	49w
27/03/26	3	Re-Tender Stage One	6.2w
20/04/26	4	Evaluate & Recommend	3.2w
30/04/26	5	Councillor Briefing	0.4w
06/05/26	6	Council Decision	0d
11/05/26	7	Appoint Stage One Designer	0d
04/09/26	8	Stage 1 Design & Costing	16w
23/10/26	9	Prepare Consultation + Pre-publicity	35d
01/01/27	10	Public Consultation	9w
01/02/27	11	Analysis & Reporting	4.2w
10/02/27	12	Council Decision	0d
30/04/27	13	Neighbourhood CIL Windows	16w
30/04/27	14	District CIL Window	26w
04/04/28	15	BNG Funding & Other Grants	58.4w
26/07/27	16	Stage 2 Design & Tender	20.2w
	17	Select Contractor	
	18	Place Order	
	19	Statutory Approvals	
	20	Securing Funds	
	21	Pincipal Works on Site
